FOR DESIGN AND CONSTRUCTION

THE DIVINE ART: 4 Centuries of European Tapestries

REGENSTEIN GALLERY

Tapestry_schedule_in_Fasttrac

7/30/08
2nd draft
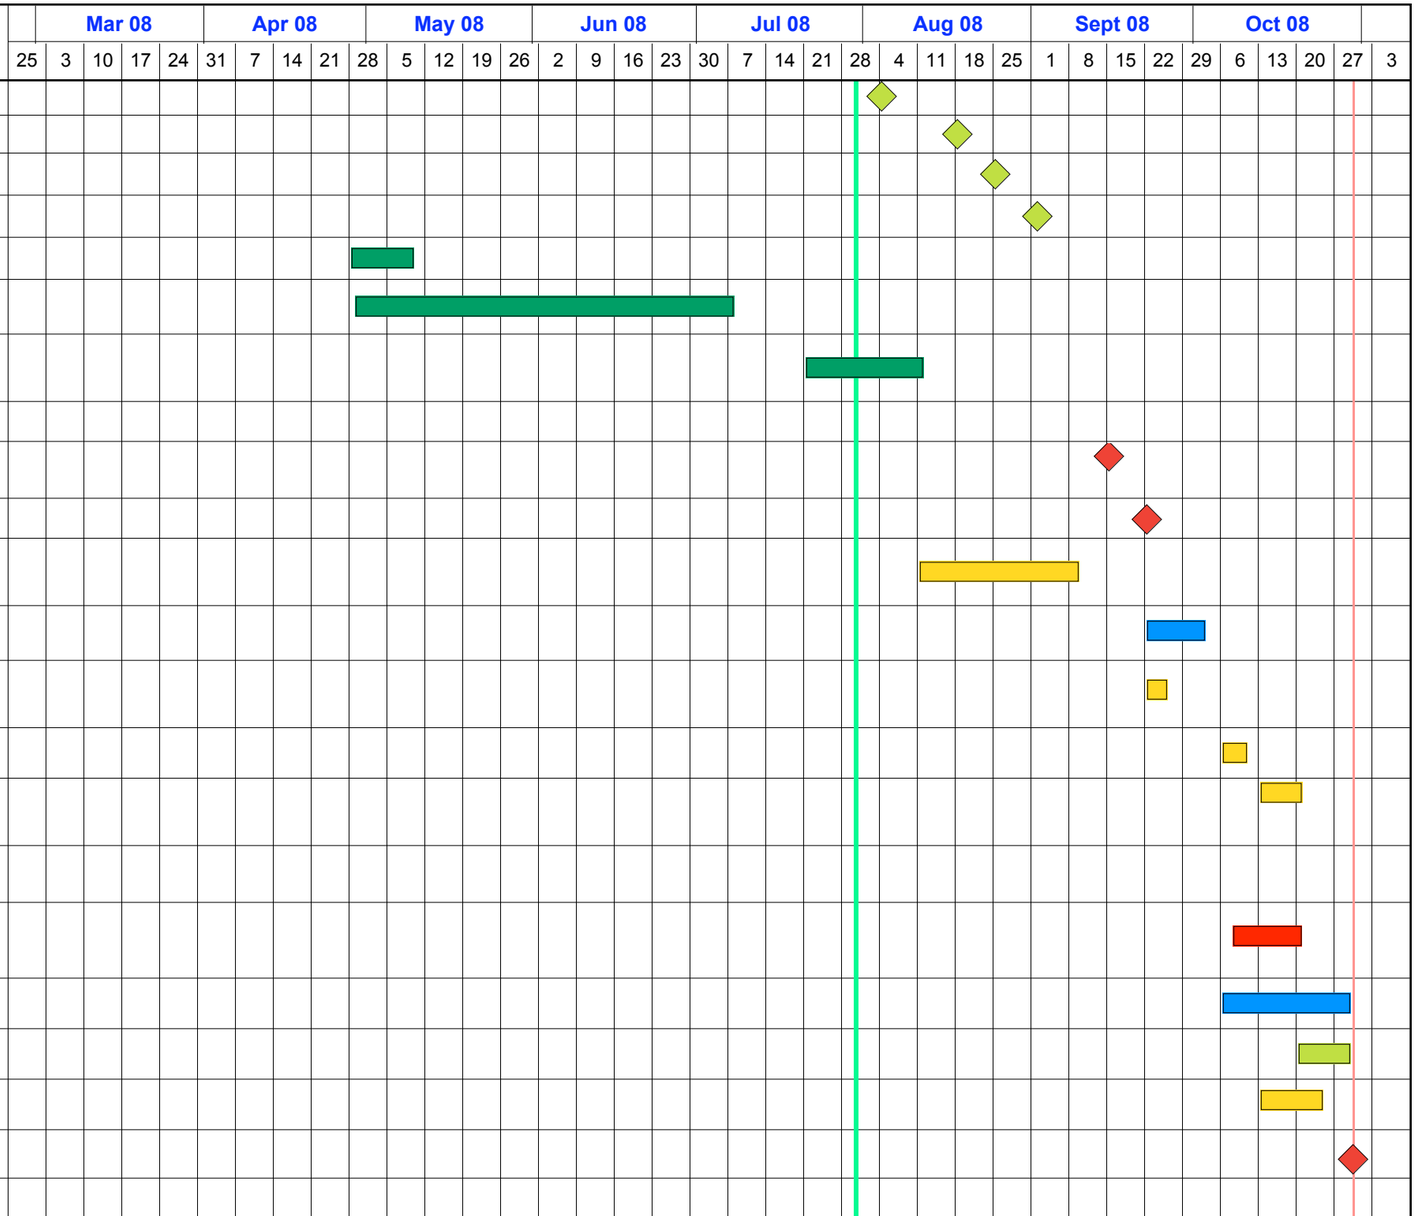
	Activity Name	Depart.	Start Date	Finish Date
1	To Graphics: Maps & photomurals		**8/4/08**	**8/4/08**
2	To Graphics: Text Panels		**8/18/08**	**8/18/08**
3	To Graphics: Labels		**8/25/08**	**8/25/08**
4	To Graphics: Exhibition Title/Credits		**9/2/08**	**9/2/08**
5	Space planning	D&C	**4/28/08**	**5/9/08**
6	Plans, Elevations, and Detail drawings,	D&C	**4/29/08**	**7/7/08**
7	Exhibit Design Sign Offs, Construction Docs to DoPP	D&C	**7/21/08**	**8/11/08**
8	Exhibit Team Overview Meeting			
9	New Light Closes Sept. 14, 2008		**9/15/08**	**9/15/08**
10	Benin Closes Sept 21, 2008	AAA	**9/22/08**	**9/22/08**
11	Carpentry, Stanchions, & Platforms, Textile supports, Shop work	DoPP	**8/11/08**	**9/9/08**
12	Art Handlers de-install Benin	Registration	**9/22/08**	**10/2/08**
13	DoPP--Gallery 267 paint walls and platforms	DoPP	**9/22/08**	**9/25/08**
14	DoPP--1st Half week of October 6	DoPP	**10/6/08**	**10/10/08**
15	DoPP--2nd Half week of October 13 thru Oct 20	DoPP	**10/13/08**	**10/20/08**
16	Prep objects/ Mounts (TBD)			
17	I.T. Tech. as needed for cases and platforms	I.T.	**10/8/08**	**10/20/08**
18	Install Tapestry--starting Oct 6	Textiles	**10/6/08**	**10/29/08**
19	Labels and Graphics Installation	Graphics	**10/20/08**	**10/29/08**
20	Install Stanchions, touch up walls		**10/13/08**	**10/24/08**
21	Press Opening/Member Preview	Textiles	**10/30/08**	**10/30/08**
22	Open to Public Nov. 1 Saturday
